

Austrian Cultural Heritage
200 Years Cadastre



Land Registers Interconnection portal: When will it happen?

CVC2017

Rik Wouters
Managing Director EULIS
Vienna, Austria
October 5-6 2017

www.eulis.eu

Topics



Land Registers Interconnection (LRI)

State of affairs in EULIS

www.eulis.eu

LRI system: online access through the e-Justice Portal



The screenshot shows the European e-Justice Portal interface. On the left, a vertical menu lists various legal topics. An orange arrow labeled '1' points to the 'Registers' link in this menu. The 'Registers' link is highlighted with a mouse cursor. To the right of the menu, a large blue box contains the heading 'General information on business, land and insolvency registers at EU and Member State level'. Below this heading, the 'Registers' section is expanded, showing three categories: 'Business registers', 'Land registers', and 'Insolvency registers'. An orange arrow labeled '2' points to the 'Land registers' category. The 'Land registers' category lists 'Land registers at European level' and 'Land registers in Member States'. The 'Insolvency registers' category lists 'Interconnected insolvency registers search'.



Registers

- Business registers**
 - Business registers at European level
 - Business registers in Member States
- Land registers**
 - Land registers at European level
 - Land registers in Member States
- Insolvency registers**
 - Interconnected insolvency registers search

LRI-ELS-IMOLA



Extend service (3/3)
Future: Map entry facility

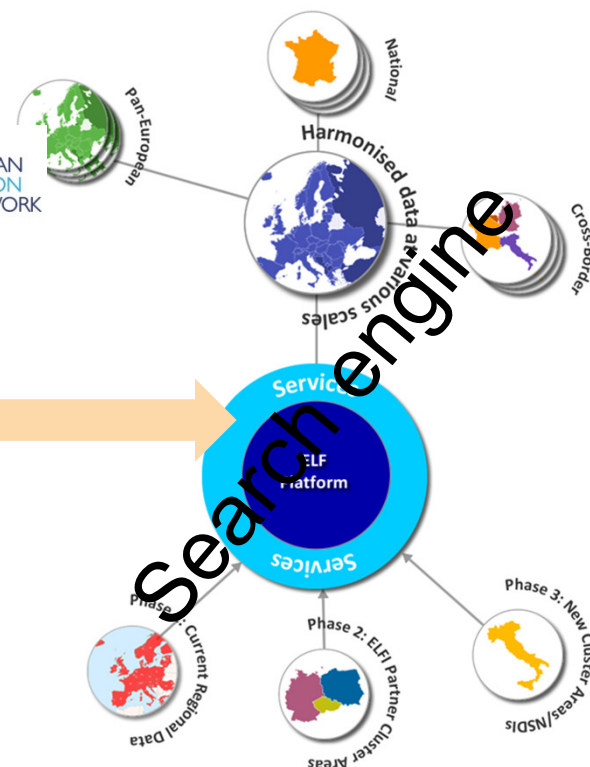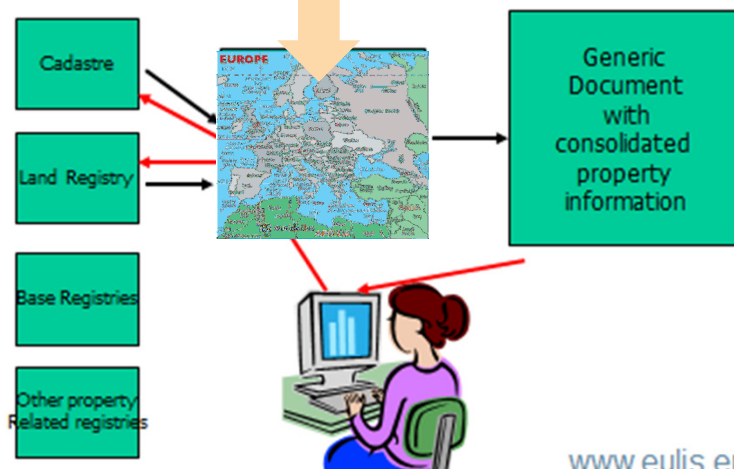

Overview milestones



1. Feasibility report on Interconnection, September 2014
2. 18 EU countries support initiative and 12 wish to connect, Dec 2014
3. Decision of WP e-Justice EULIS as basis for the Solution! January 2015
4. Decision Commission to start project, September 2015
5. High level architecture and functionality ready, January 2016
6. Two expert meetings, January and October 2016
7. Working group established to be closer to Commission, February 2017
8. Working group prepared comments on the portal design, April 2017

www.eulis.eu

Timing plan LRI

ID	Milestone Description	Target Delivery Date
1	End of <i>Initiating</i> phase: Business Case, Project Charter approved	Q1 2016 ✓
1.5	Signature of contract with winning consortium	Q2 2016 ✓
2	Delivery of initial mock-up prototype	Q3 2016 ✓
3	End of <i>Planning</i> phase I: certain planning artefacts approved	Q1 2017 → Q2 2017 ✓
3.1	Start of <i>Executing</i> phase I	Q1 2017 → Q2 2017 ✓ ?
3.2	Start of <i>Planning</i> phase II: integration of PSP / maps (ELS)	Q1-2 2017 → Q4 2017?
3.3	Start of <i>Executing</i> phase II	Q2 2017 → Q1 2018?
4	Delivery of application in TEST env. (end of <i>executing</i> phase I)	Q2 2017 → Q4 2017?
4.1	Delivery of application in TEST env. (end of <i>executing</i> phase II)	Q2-3 2017 ??

Timing plan LRI

ID	Milestone Description	Target Delivery Date
5	Deployment of application in ACCEPTANCE environment	Q3 2017 → Q1 2018
6	Acceptance of DIGIT test results (STRESS, VULNERABILITY)	Q3 2017 → Q1 2018
7	Finalisation of integration testing (Phase I)	Q3-Q4 2017 → Q2 2018
8	End of <i>Closing</i> phase: all deliverables are accepted	Q3-Q4 2017 ???

Wrap up

- Integration with national portal can start from May 2018?
- Connection most likely not before end 2018 for AT and EE
- End of phase II will not before be January 2019
- Connection portal (including payment facility) by mid 2019?

Our observations

Issue list presented to the Commission:

- Authentication/authorisation: circle of trust!!
- Payment facility: no clarity on solution
- Reference Information/glossary
- User-dialogue more complex and less agile than in EULIS

Since April 2017 no formal response from Commission

Conclusions

- Delay in planning considerable: tangible progress last year almost zero
- Change of project manager caused severe disruption
- Payment service a real obstacle and risk
- Interest in connection faded away since 2015

NB Is delay not a bad omen for the successful completion of the project?


State of Play EULIS

Organisation EULIS

20 member countries

Board composition:

- Pekka Halme Chair (Finland)
- Peter Hoogwerf (Netherlands)
- James O'Boyle (Ireland)
- Anders Sandin (Sweden)

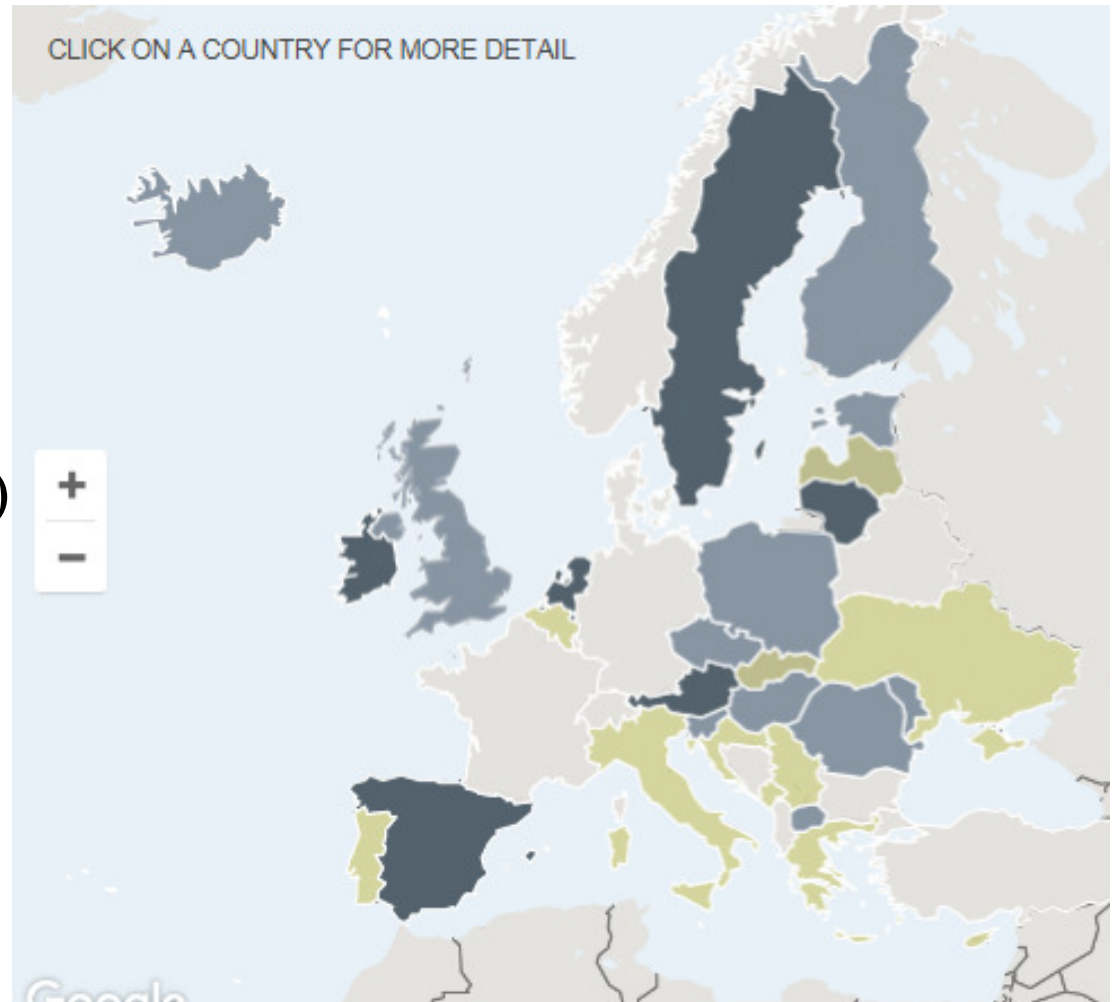

Annual member meeting



April 2017 Gavle Sweden



Future of EULIS



Do we still need EULIS as organisation?

Now the new LRI-portal will be launched

Decisions of the members:

- Close down the portal
- No need for EULIS: abolish the organisation

But also:

- Establish User Group LRI

www.eulis.eu

Priorities 2017

To close down EULIS organisation

- Plan for all activities: ready in August 2017
- Implementation in progress

Main milestones:

- Portal closed, June 2017 (done)
- New user group established
- Website will be closed, January 1st 2018
- All formalities finished, March 2018

New User Group LRI



Tasks User Group LRI:

- Support Land Registers Interconnection project
- Stimulate land registries to connect to the LRI-portal
- Support countries technically to connect to LRI
- Represent connected countries in “Brussels”
- Exchange experiences among connected countries

Who will do the coordination? NL Kadaster

Who can become member? All European countries

www.eulis.eu

Thank you for your excellent support and cooperation!



Info: rik.wouters@kadaster.nl

www.eulis.eu
